

MIXED-USE COMMERCIAL DEVELOPMENT

12,000 m² | 2 FLOORS + 2 BASEMENT PARKING

RETAIL • OFFICES • ENTERTAINMENT • RESTAURANTS • CAFÉS • PARKING



3
ZONES



5
MAIN CONTRACTORS



12,000 m²
TOTAL AREA



PROJECT OVERVIEW

-  Location
Saudi Arabia
-  Total Area
12,000 m²
-  Levels
2 Floors + 2 Basement
-  Project Type
Mixed-Use Commercial
-  Components
Retail, Offices, Entertainment,
Restaurants, Cafés, Parking

PROJECT ZONES



KEY CHALLENGES

-  Weak funding and cash-flow constraints
-  Quality issues and rework (Main Facade)
-  Actual progress lower than planned
-  Uneven performance between contractors and zones

RETAIL AREA



FOOD COURT



ENTERTAINMENT ZONE



OFFICE SPACES



PARKING BASEMENT



KEY OUTCOMES



Overall Progress
Planned: 100%
Actual: 82%
Gap: -18%



Rework Reduction
-32%
(After corrective actions)



On-Time Handover
+17%
Improvement in zone handover readiness



Contractor Performance
Improved by
21%
on average



Dashboard Visibility
Real-time tracking and data-driven decision making

TOOLS & TECHNOLOGY



CONSTRUCTION ANALYTICS CASE STUDY

MIXED-USE COMMERCIAL DEVELOPMENT

12,000 m² | 2 FLOORS + 2 BASEMENT PARKING

RETAIL • OFFICES • ENTERTAINMENT • RESTAURANTS • CAFÉS • PARKING


- Location: Saudi Arabia
- Total Area: 12,000 m²
- Levels: 2 Floors + 2 Basement
- Project Type: Mixed-Use Commercial
- Main Contractors: 5 Contractors
- Execution Zones: 3 Zones

PROJECT ZONES



1) CONTRACTOR PERFORMANCE (PIE CHART)

ACTUAL PROGRESS % FROM TOTAL SCOPE

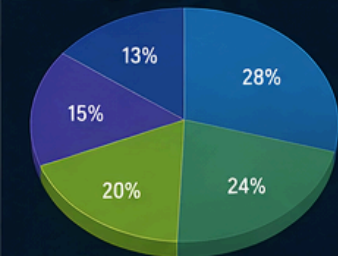

CONTRACTOR	SCOPE %	ACTUAL %
Contractor A	28%	62%
Contractor B	24%	58%
Contractor C	20%	66%
Contractor D	15%	55%
Contractor E	13%	48%

Overall Average Progress: 64%

CONTRACTOR DETAILED PERFORMANCE

CONTRACTOR	SCOPE %	PLANNED %	ACTUAL %	PROGRESS GAP	DELAY (DAYS)	QUALITY (REWORK %)
Contractor A	28%	86%	62%	-24%	32	4.2%
Contractor B	24%	83%	58%	-25%	30	3.1%
Contractor C	20%	85%	66%	-19%	18	3.6%
Contractor D	15%	81%	55%	-26%	35	4.8%
Contractor E	13%	80%	48%	-32%	45	5.0%

KEY KPIs

OVERALL PROGRESS
(PLANNED vs ACTUAL)



REWORK COST
(QUALITY ISSUES)



AVG DELAY
(DAYS)




ON-TIME HANDOVER
(READY ZONE)



PRODUCTIVITY
(OVERALL)



2) ZONE WISE PROGRESS (COLUMN CHART)

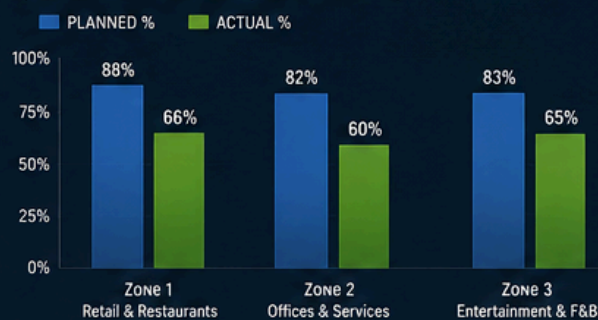

TOP DELAYED ACTIVITIES

ACTIVITY	ZONE	DELAY (DAYS)	IMPACT
Facade Cladding Works	1	45	High
Interior Finishes - Shops	1	38	High
Ceiling & MEP Finishes	2	32	Medium
Flooring Works	2	28	Medium
Joinery & Fixtures	3	25	Medium

KEY INSIGHTS

- Funding delays directly impacted material procurement and contractor productivity.
- Rework on main facade caused cost overrun and affected overall progress.
- Zone 2 (Offices) is the most behind schedule due to slow finishes and approvals.
- Contractor E is the most delayed and requires immediate corrective actions.


OUTCOMES & IMPACT

- Improved visibility of project performance across all zones and contractors
- Better decision making based on real data and trend analysis
- Focused action on delayed activities reduced further delays
- Expected improvement in on-time handover and overall project quality


PROJECT CHALLENGES

- Weak funding and cash-flow constraints
- Quality issues and rework (Main Facade)
- Actual progress lower than planned
- Uneven performance between contractors and zones

PROJECT DELAY ANALYSIS (FUNNEL)

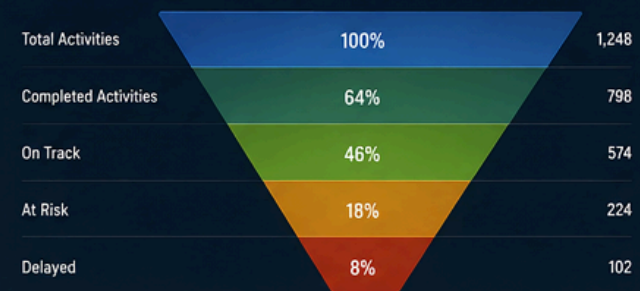

3) PLANNED vs ACTUAL PROGRESS OVER TIME (LINE CHART)

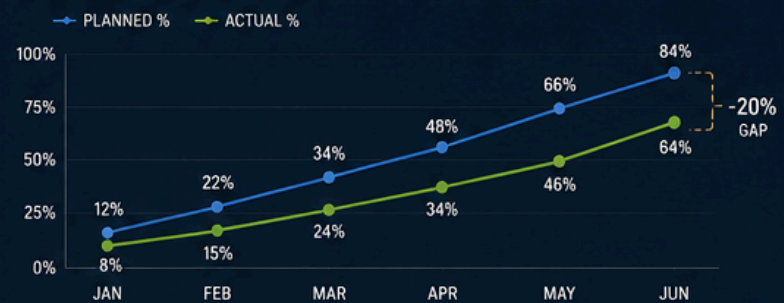

TOOLS & TECHNOLOGY

- Power BI
 - Excel
 - SQL
- Data Collection: Daily Progress Reports, Site Inspections, Contractor Submissions, ERP & Document Tracking
